

NAME:AVINASH JULAKATTI

SRN:PES1UG24AM347

SECTION:F

The screenshot shows the Jira interface for the 'SSL board' (Space: SSL-Alert-PES1UG24AM347). The 'Backlog' tab is selected. The 'SSL Sprint 1' section is empty, with a 'Plan your sprint' message: 'Drag work items from the Backlog section or create new ones to plan the work for this sprint. Select Start sprint when you're ready.' Below this, the 'Backlog' section is also empty, with the message 'Your backlog is empty.' The left sidebar shows the 'SSL board' selected under 'Recent' spaces.



The screenshot shows the Jira interface for the 'SSL board' with the 'Backlog' tab selected. The backlog now contains 12 work items. The 'Epic' filter is applied, showing three epics: 'Epic 1: Domain & Certificate Monitoring Engine', 'Epic 2: Expiry Alerting & Escalation', and 'Epic 3: Dashboard, Audit Log & Access Control'. The backlog items are listed with their IDs, titles, and associated epics. The 'SSL Sprint 1' section is still empty.

ID	Title	Epic	Status	Estimate	Assignee
SSL-4	Story 1.1: Register Domain for Monitoring	Epic 1: Do...	To Do	3	
SSL-5	Story 1.2: Retrieve SSL Expiry via TLS Handshake	Epic 1: Do...	To Do	5	
SSL-6	Story 1.3: Retrieve Domain Expiry via WHOIS	Epic 1: Do...	To Do	5	
SSL-7	Story 1.4: Scheduled Daily Audit at 00:00 UTC	Epic 1: Do...	To Do	8	
SSL-8	Story 1.5: Retry and Mark Domain Unreachable	Epic 1: Do...	To Do	3	
SSL-9	Story 2.1: Threshold Email Alerts (30/15/3 Days)	Epic 2: Ex...	To Do	5	
SSL-10	Story 2.2: Acknowledge an Alert	Epic 2: Ex...	To Do	3	
SSL-11	Story 2.3: Escalate Unacknowledged Critical A...	Epic 2: Ex...	To Do	5	
SSL-12	Story 2.4: Downtime and Connection Error Alert	Epic 2: Ex...	To Do	3	
SSL-13	Story 3.1: Expiry Status Dashboard	Epic 3: Da...	To Do	8	
SSL-14	Story 3.2: Audit Run Log	Epic 3: Da...	To Do	3	
SSL-15	Story 3.3: Role-Based Access Control	Epic 3: Da...	To Do	5	

The screenshot shows a close-up of the 'SSL Sprint 1' section, which now contains 5 work items. The items are listed with their IDs, titles, and associated epics. The 'SSL-9' item is highlighted.

ID	Title	Epic	Status	Estimate	Assignee
SSL-4	Story 1.1: Register Domain for Monitoring	Epic 1: Do...	To Do	3	
SSL-5	Story 1.2: Retrieve SSL Expiry via TLS Handshake	Epic 1: Do...	To Do	5	
SSL-6	Story 1.3: Retrieve Domain Expiry via WHOIS	Epic 1: Do...	To Do	5	
SSL-7	Story 1.4: Scheduled Daily Audit at 00:00 UTC	Epic 1: Do...	To Do	8	
SSL-9	Story 2.1: Threshold Email Alerts (30/15/3 ...	Epic 2: Ex...	To Do	5	




NAME:AVINASH JULAKATTI
SRN:PES1UG24AM347
SECTION:F

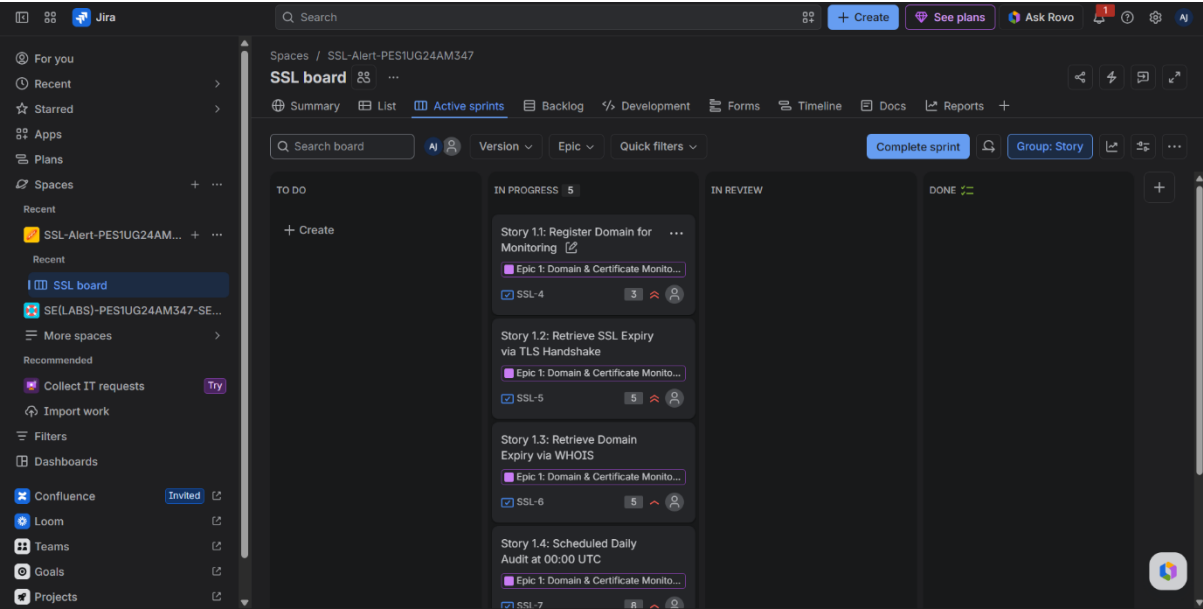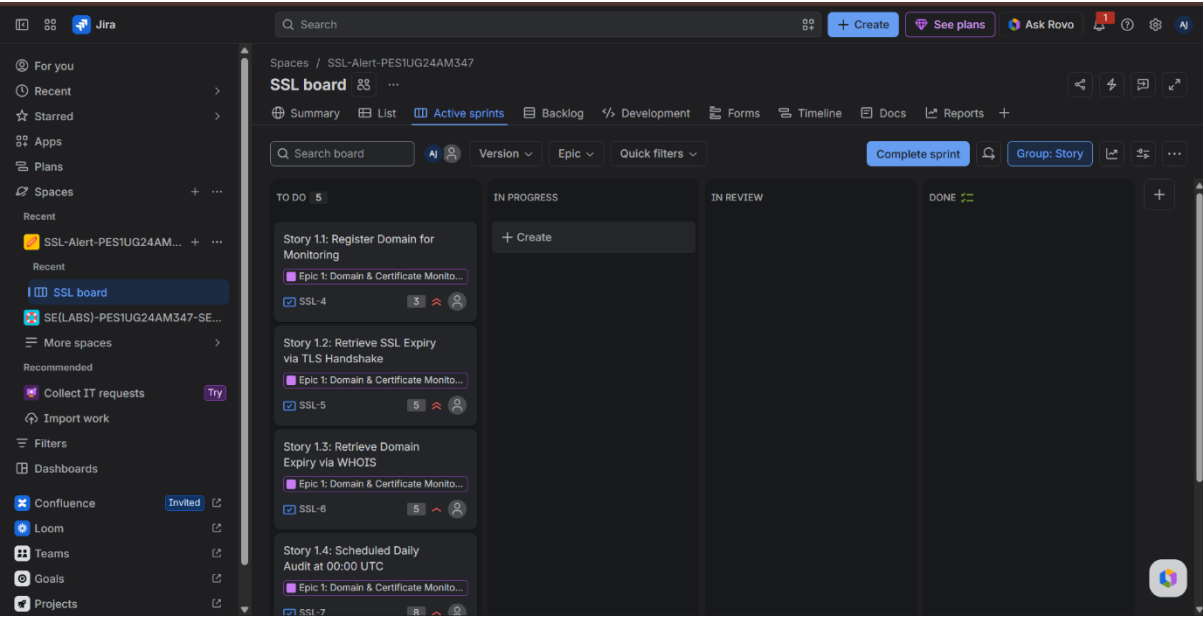



NAME:AVINASH JULAKATTI

SRN:PES1UG24AM347


SECTION:F

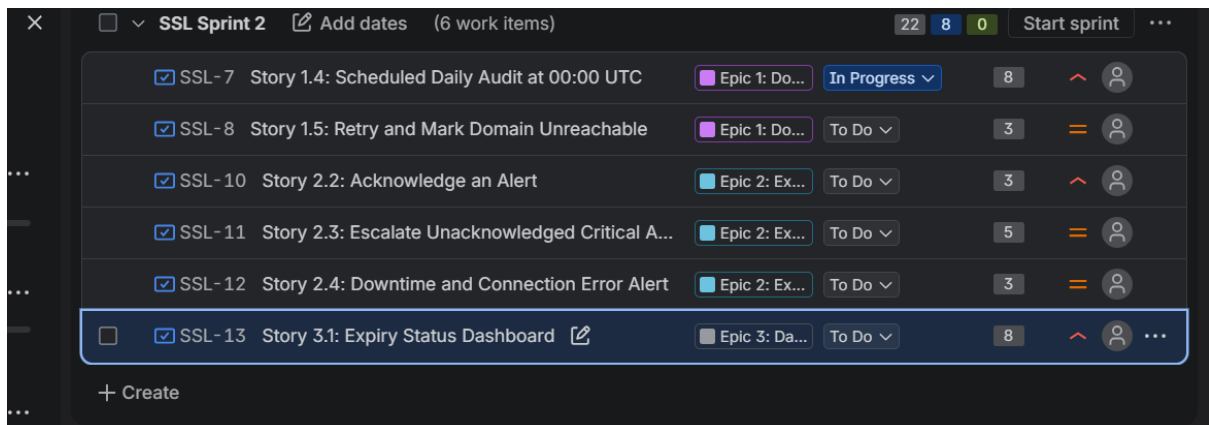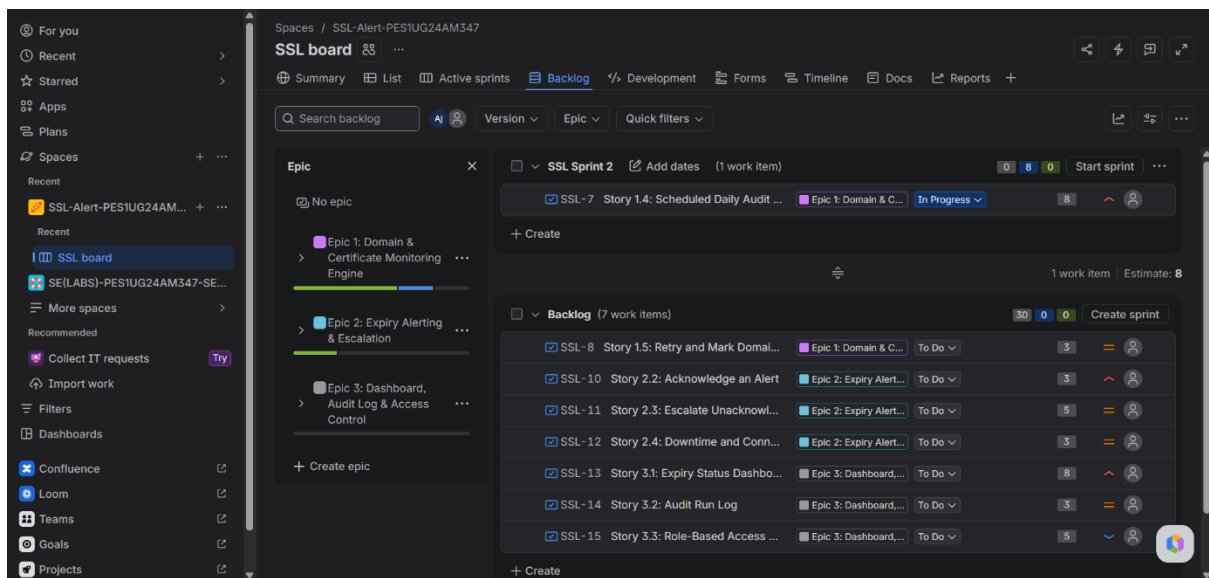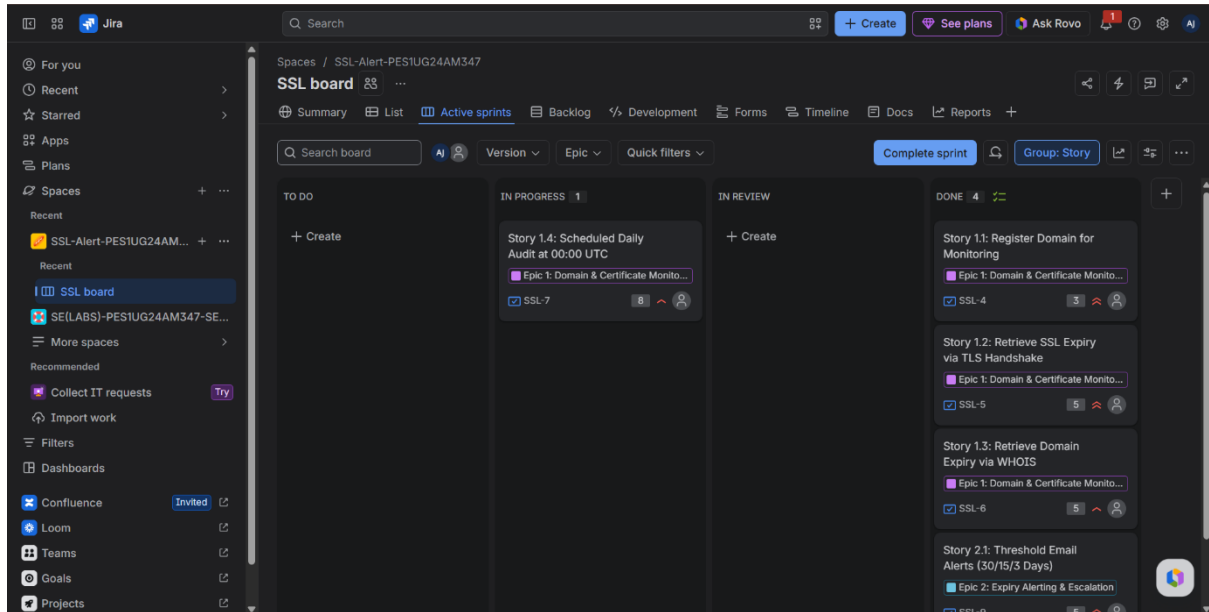

NAME:AVINASH JULAKATTI
SRN:PES1UG24AM347
SECTION:F

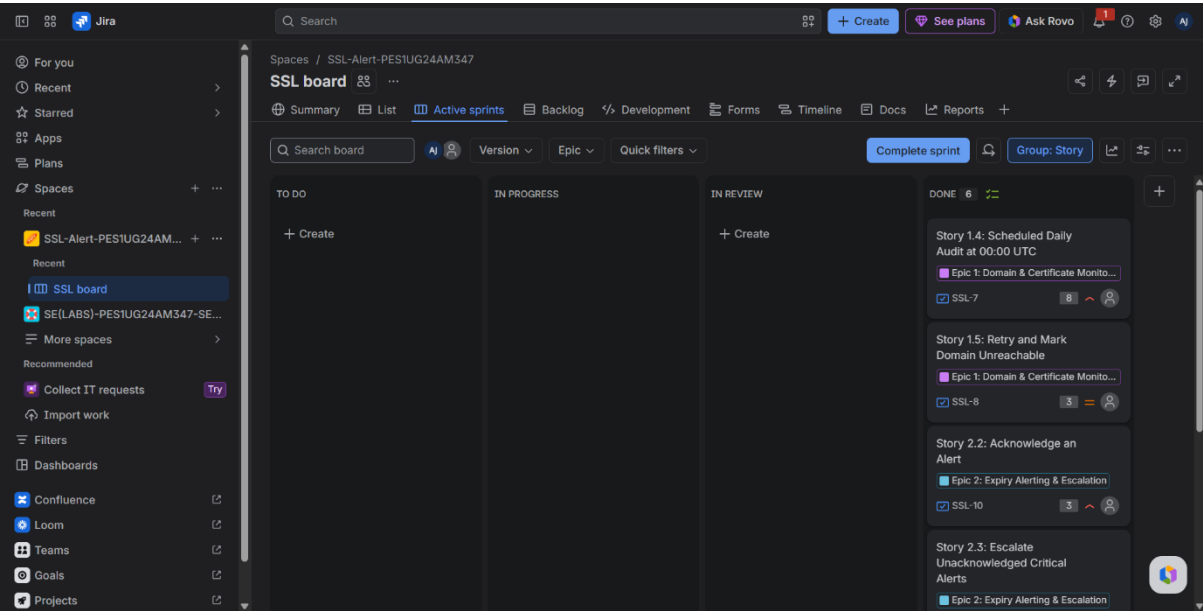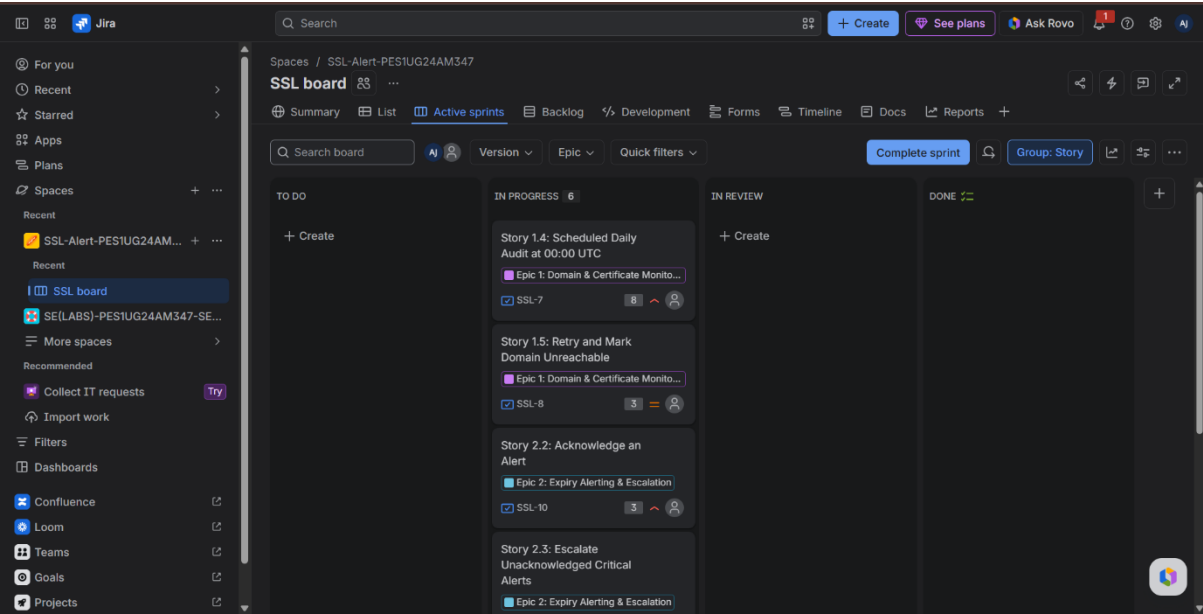

NAME:AVINASH JULAKATTI
SRN:PES1UG24AM347
SECTION:F

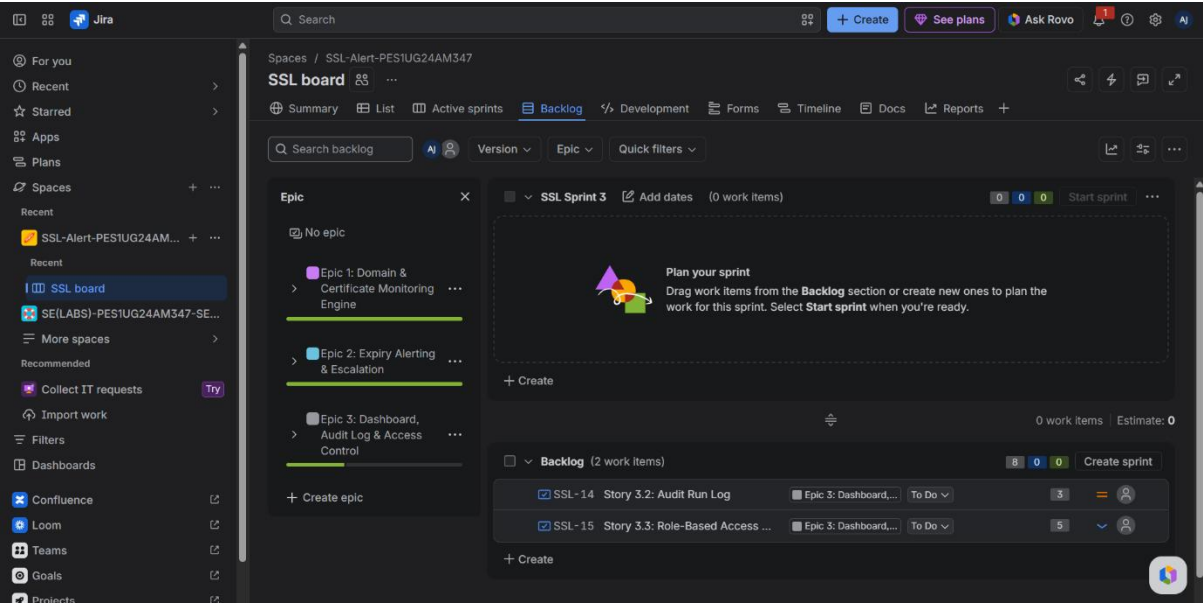

NAME:AVINASH JULAKATTI
SRN:PES1UG24AM347
SECTION:F

For you

Recent

Starred

Apps

Plans

Spaces

Recent

SSL-Alert-PES1UG24AM...

SSL board

SE(LABS)-PES1UG24AM347-SE...

More spaces

Recommended

Collect IT requests

Import work

Filters

Dashboards

Confluence

Loom

Teams

Goals

Projects

Spaces / SSL-Alert-PES1UG24AM347

SSL board

SummaryListActive sprintsBacklogDevelopmentFormsTimelineDocsReports

Search backlog

Version

Epic

Quick filters

Epic

SSL Sprint 3

Add dates

0 work items

000Start sprint

Plan your sprint

Drag work items from the Backlog section or create new ones to plan the work for this sprint. Select Start sprint when you're ready.

Create

0 work items | Estimate: 0

Backlog (2 work items)

800Create sprint

SSL-14Story 3.2: Audit Run LogEpic 3: Dashboard...To Do3

SSL-15Story 3.3: Role-Based Access ...Epic 3: Dashboard...To Do5

Create

For you

Recent

Starred

Apps

Plans

Spaces

Recent

SSL-Alert-PES1UG24AM...

SSL board

SE(LABS)-PES1UG24AM347-SE...

More spaces

Recommended

Collect IT requests

Import work

Filters

Dashboards

Confluence

Loom

Teams

Goals

Projects

Spaces / SSL-Alert-PES1UG24AM347

SSL board

SummaryListActive sprintsBacklogDevelopmentFormsTimelineDocsReports

Search backlog

Version

Epic

Quick filters

Epic

SSL Sprint 3

Add dates

0 work items

000Start sprint

Plan your sprint

Drag work items from the Backlog section or create new ones to plan the work for this sprint. Select Start sprint when you're ready.

Create

0 work items | Estimate: 0

Backlog (2 work items)

800Create sprint

SSL-14Story 3.2: Audit Run LogEpic 3: Dashboard...To Do3

SSL-15Story 3.3: Role-Based Access ...Epic 3: Dashboard...To Do5

Create

For you

Recent

Starred

Apps

Plans

Spaces

Recent

SSL-Alert-PES1UG24AM...

SSL board

SE(LABS)-PES1UG24AM347-SE...

More spaces

Recommended

Collect IT requests

Import work

Filters

Dashboards

Confluence

Loom

Teams

Goals

Projects

Spaces / SSL-Alert-PES1UG24AM347

SSL board

SummaryListActive sprintsBacklogDevelopmentFormsTimelineDocsReports

Search backlog

Version

Epic

Quick filters

Epic

SSL Sprint 3

Add dates

0 work items

000Start sprint

Plan your sprint

Drag work items from the Backlog section or create new ones to plan the work for this sprint. Select Start sprint when you're ready.

Create

0 work items | Estimate: 0

Backlog (2 work items)

800Create sprint

SSL-14Story 3.2: Audit Run LogEpic 3: Dashboard...To Do3


SSL-15Story 3.3: Role-Based Access ...Epic 3: Dashboard...To Do5

Create

NAME:AVINASH JULAKATTI

SRN:PES1UG24AM347

SECTION:F

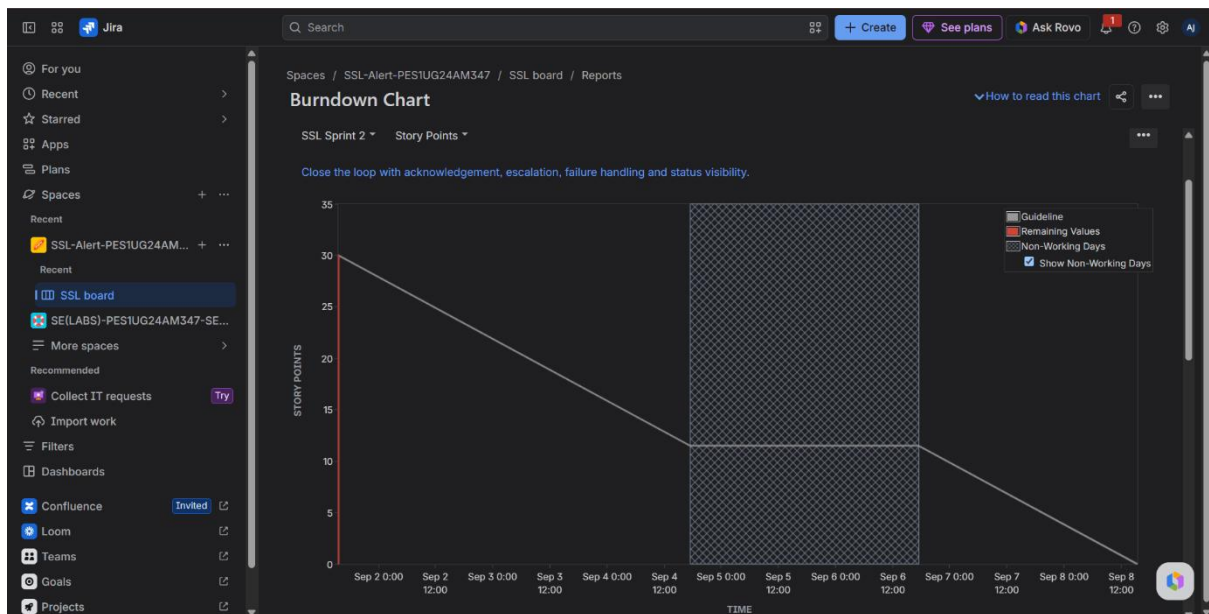

1. Did your estimations reflect the actual effort?

Partly. The small, well-understood stories were accurate — Story 1.1 (*Register Domain for Monitoring*) and Story 2.2 (*Acknowledge an Alert*), both estimated at 3 points, closed comfortably within their sprints.

The estimate that failed was **Story 1.4: Scheduled Daily Audit at 00:00 UTC**, assigned 8 points. It was the only committed item not completed in Sprint 1 and had to be carried into Sprint 2. In hindsight it bundled several distinct concerns that the Lab 1 use case had already separated: the scheduler trigger, iteration across the active domain list, per-domain retry handling, and the audit log write. It should have been split into two or three smaller stories before being pulled into a sprint.

This is precisely why the Fibonacci scale widens at the top end — the gap from 5 to 8 to 13 encodes rising uncertainty, so an 8-point estimate is better read as a warning that the item is not yet understood well enough to commit to.

NAME:AVINASH JULAKATTI

SRN:PES1UG24AM347

SECTION:F

2. Was your backlog well-prioritized?

Yes. Ordering was driven by dependency and business value rather than ease of implementation.

Story 1.2 (*SSL expiry via TLS handshake*) and Story 1.4 (*daily scheduler*) were ranked **Highest** because every downstream capability — alerting, escalation, dashboard, audit log — is worthless without an expiry date to act on. Placing Story 1.1 and Story 2.1 immediately after them meant Sprint 1 alone produced a usable end-to-end system: register a domain, detect its expiry, receive an email.

Governance features with real but non-urgent value — Story 3.2 (*Audit Run Log*) and Story 3.3 (*Role-Based Access Control*) — were ranked lowest and remain undelivered. That is a correct outcome rather than a shortfall; a well-prioritized backlog is expected to have a tail that is never reached within the planning horizon.

3. How did your simulated sprint align with your plan?

Sprint 1 diverged from plan. It committed 26 points across five stories and delivered 18 across four — a 69% completion rate, with one 8-point story rolling over.

Sprint 2 aligned exactly. It committed 30 points including the carryover and delivered all 30.

The difference was not that the second sprint contained easier work, but that it was planned against a *measured* velocity instead of an assumption. Sprint 1 had no historical data, so its commitment was a guess; Sprint 2 could be sized against the 18 points actually observed. This is the empirical feedback loop Scrum is built around, and it became visible after only a single iteration.

4. What insights did the burndown chart give about your team's capacity?

Read together with the Sprint Report, the charts indicate a sustainable capacity of roughly **18–30 story points per one-week sprint**, with 18 being the only figure actually demonstrated under first-attempt conditions.

Sprint 1 finished with 8 points unburned against a guideline that reached zero — the standard signature of over-commitment. Jira's own guidance notes that a sharp drop in the burndown often indicates work that was not estimated accurately or not broken down properly, which matches Story 1.4 precisely.

Sprint 2 burned its full 30 points, but since 8 of those were carried-over work already partly complete, the honest planning figure for a future sprint is closer to **22–25 points**.

The practical rule taken from this exercise: treat any story estimated above 8 points as a candidate for splitting before it is committed, and size each sprint against demonstrated velocity rather than optimism.
